PACK Schedule.gnt

REESMANS EXCAVATING AND GRADING INC.
South Packard Avenue Relay Schedule

#	Task name	Crew	Start date	Duration	Finish date
1	Raw Water Pabst Avenue	1st Crew	10/6/2011	5	10/12/2011
2	Holmes Intersection	1st Crew	9/26/2011	5	9/30/2011
3	Sanitary Holmes to Pulaski	2nd crew	10/3/2011	13	10/19/2011
4	Water Main Holmes to Munkwitz	1st Crew	10/3/2011	3	10/5/2011
5	Water Main Holmes to Munkwitz	1st Crew	10/12/2011	3	10/14/2011
6	Sanitary Holmes to Munkwitz	1st Crew	10/17/2011	7	10/25/2011
7	Laterals and Storm	2nd Crew	10/20/2011	14	11/8/2011
8	Storm Pabst	1st Crew	10/26/2011	2	10/27/2011
9	Water Main Pabst to Barnard	1st Crew	10/28/2011	7	11/7/2011
10	Sanitary Sewer Pabst to Barnard	1st Crew	11/8/2011	5	11/14/2011
11	Laterals Pabst to Munkwitz	2nd Crew	11/9/2011	5	11/15/2011
12	Storm Sewer Squire to Lirary	1st Crew	11/15/2011	7	11/23/2011
13					
14	Water Main Barnard to Layton	1st Crew	3/5/2012	5	3/9/2012
15	Sanitary Layton to Barnard	1st Crew	3/12/2012	9	3/22/2012
16	Storm Sewer Squire to Layton	1st Crew	3/23/2012	5	3/29/2012
17	Laterals Munkwitz to Layton	2nd Crew	3/30/2012	16	4/20/2012
18	Water Main Layton to Plankington	1st Crew	3/30/2012	7	4/9/2012
19	Sanitary Layton to Cudahy	1st Crew	4/10/2012	7	4/18/2012
20	Laterals Layton to Plankington	1st Crew	4/19/2012	4	4/24/2012
21					
22					

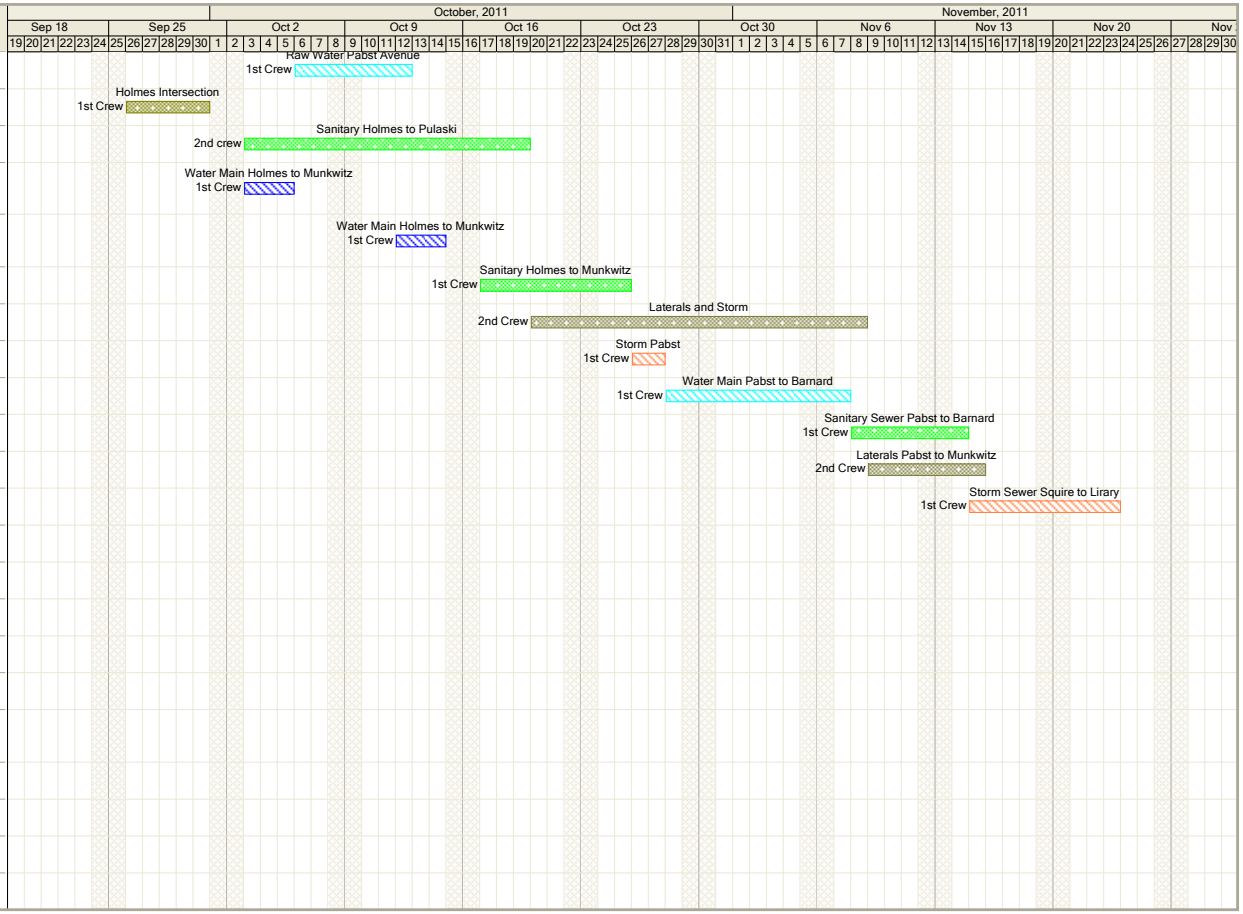

Project Manager: Adam Reesman 262-206-2673
Superintendent: Joe Kresken 262-206-0615
Foreman: Tony Gerulat : 262-206-0620

8/23/2011

PACK Schedule.gnt

REESMANS EXCAVATING AND GRADING INC.
South Packard Avenue Relay Schedule

#	Task name	Crew	Start date	Duration	Finish date
1	Raw Water Pabst Avenue	1st Crew	10/6/2011	5	10/12/2011
2	Holmes Intersection	1st Crew	9/26/2011	5	9/30/2011
3	Sanitary Holmes to Pulaski	2nd crew	10/3/2011	13	10/19/2011
4	Water Main Holmes to Munkwitz	1st Crew	10/3/2011	3	10/5/2011
5	Water Main Holmes to Munkwitz	1st Crew	10/12/2011	3	10/14/2011
6	Sanitary Holmes to Munkwitz	1st Crew	10/17/2011	7	10/25/2011
7	Laterals and Storm	2nd Crew	10/20/2011	14	11/8/2011
8	Storm Pabst	1st Crew	10/26/2011	2	10/27/2011
9	Water Main Pabst to Barnard	1st Crew	10/28/2011	7	11/7/2011
10	Sanitary Sewer Pabst to Barnard	1st Crew	11/8/2011	5	11/14/2011
11	Laterals Pabst to Munkwitz	2nd Crew	11/9/2011	5	11/15/2011
12	Storm Sewer Squire to Lirary	1st Crew	11/15/2011	7	11/23/2011
13					
14	Water Main Barnard to Layton	1st Crew	3/5/2012	5	3/9/2012
15	Sanitary Layton to Barnard	1st Crew	3/12/2012	9	3/22/2012
16	Storm Sewer Squire to Layton	1st Crew	3/23/2012	5	3/29/2012
17	Laterals Munkwitz to Layton	2nd Crew	3/30/2012	16	4/20/2012
18	Water Main Layton to Plankington	1st Crew	3/30/2012	7	4/9/2012
19	Sanitary Layton to Cudahy	1st Crew	4/10/2012	7	4/18/2012
20	Laterals Layton to Plankington	1st Crew	4/19/2012	4	4/24/2012
21					
22					

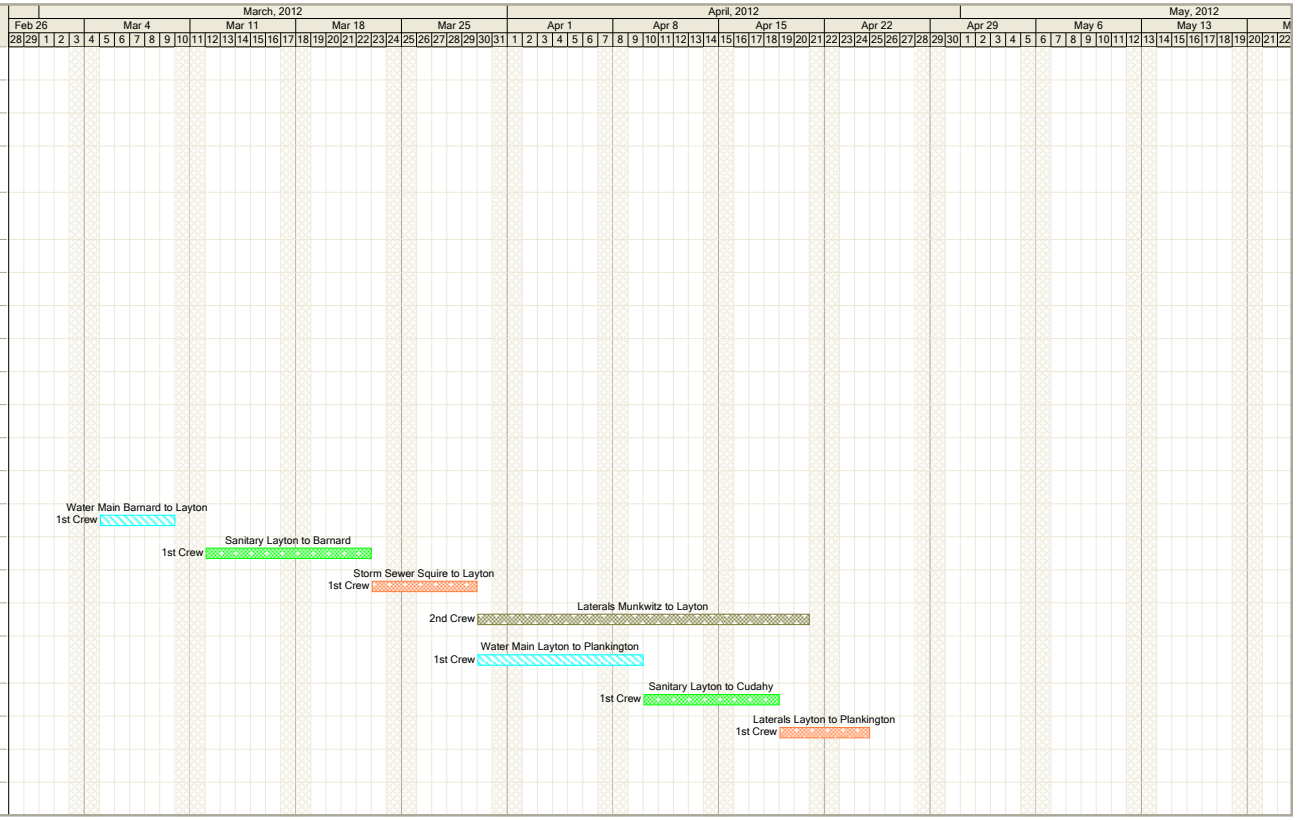

Project Manager: Adam Reesman 262-206-2673
Superintendent: Joe Kresken 262-206-0615
Foreman: Tony Gerulat : 262-206-0620

8/23/2011
